

Home Inspection Report

Prepared For: Sample Home Inspection Report



Confidential, Ohio

Maintenance Summary

This summary is not the entire report. The complete report may include additional information of concern to the client. It is recommended that the client read the complete report.

Roof

1. West Chimney Chimney: Brick - Chimney crown cracked and should be repaired by a reputable chimney or roofing contractor.

Exterior

- 2. Gas Meter: Exterior surface mount at left side of home Clear out vegetation all around the meter. Lots and Grounds
- 3. Walks and steps: Concrete Some erosion observed on the front steps. This can be repaired by a reputable mason.
- 4. Vegetation: Trees and shrubs and low vegetation on the perimeter of the home Trim trees and shrubs away from the structure at least 10-12". Recommend landscape contractor.

Air Conditioning

 Left side of home AC System A/C System Operation: Functional today - Recommend reputable licensed HVAC contractor tune-up as no regular servicing evidence was found. Average life of a unit is 15 years. Budget for replacement.

Heating System

- 6. Basement Heating System Heating System Operation: Functional the day of the inspection Working fine today. Recommend a licensed HVAC contractor tune-up as the last service on the service tag was 5 years ago.
- 7. Basement Heating System Filter: Aprilaire Change filter after you are done moving in. It's due.
- 8. Basement Heating System Humidifier: April-Aire Did not come on when tested. Recommend a licensed HVAC contractor repair and change out the water panel pad.

Minor Summary

This summary is not the entire report. The complete report may include additional information of concern to the client. It is recommended that the client read the complete report.

Roof

1. West Chimney Flue/Flue Cap: Clay - Recommend adding rain/snow cap to round liner at left in picture above in Chimney section.

Exterior

- 2. Trim, fascia and soffits: Wood Peeling paint and possible wood rot or damage to the right hand dormer bottom window frame piece shown. Recommend replacing. (Handyman)
- 3. Siding: Aluminum siding Recommend handyman repair loose siding shown. A yellow jacket nest was inside the upper siding piece so a specialist may be required to remove the nest and its habitants first and then have the siding repaired. (Handyman and pest specialist)

Lots and Grounds

4. Driveway: Concrete - Driveway is in great shape from apron to garage. Observed a crack by the doors that can be filled with a good quality filler from a DIY store. This will keep the cracks from spreading and deterioration from the freeze - thaw cycles in the winter.

Garage/Carport

- 5. Attached Garage Garage Doors: Aluminum Recommend replacing bottom door seals on both doors that are cracked. (Handyman)
- 6. Attached Garage Door Openers: Wayne Dalton Consider changing out the button to a new one that has all of the parts present. (Handyman)
- 7. Attached Garage Doors and windows: Man door to outside has a lock that is inoperative and the door cannot be locked. Recommend repair or replace. (Handyman)

Kitchen

- 8. 1st Floor Kitchen Dishwasher: General Electric Properly secure to counter/base cabinets. (Handyman)
- 1st Floor Kitchen Sink plumbing: Spray hose has kinked hose at bottom as shown and should be replaced. The counter weight can then be repositioned so it will suck the hose up into the receiver better than it does now. (Licensed plumber)

Bathroom

- 10. All unless otherwise noted Bathroom Tubs, hot/cold water, drains: When both hot and cold are turned on the aereator shoots the water to the rear. It probably just needs cleaned. (Handyman)
- 11. All unless otherwise noted Bathroom Toilets: The toilet is loose at the floor (front right bedroom bathroom) and will require seal replacement and reinstallation. Fill valve needs replaced as it is spraying water out of the top seal area. (Licensed plumber)

Bedroom

12. All unless noted otherwise Bedroom Ceiling, walls and floor: Carpet burps and seams can be corrected by a carpet professional. The carpet appears to have little wear. Recommend having it stretched and then steam cleaned. Much less cost than replacing it!

Minor Summary (Continued)

Basement
13. Main Basement Windows: Single pane-metal frame - Cracked glass on basement window shown. Recommend
reputable contractor quote on repair/replace.

Major Summary

 Deck: Stained wood - Consider power washing and staining/painting next season. Steps are a couple inches too high and there are no safety railings present. (Safety item)(Handyman) Garage/Carport

2. Attached Garage Electrical: 110 VAC GFCI - Replace switch cover to switch located in the attic space above garage. (Safety item) (Handyman)

Living Space

- 3. All unless noted otherwise Living Space Doors, windows and trim: Window in first floor office will not stay up and is a safety hazard. Use caution raising and lowering the window until it get repaired or replaced. (Safety item) (Handyman)
- 4. All unless noted otherwise Living Space Smoke Detector: Hard wired Replace any unit over 10 years old even if they test ok as the sensors become unreliable. (Safety item)

Bedroom

5. All unless noted otherwise Bedroom Electrical: 110 VAC - Replace switch cover shown in bedroom. (Safety item) Basement

6. Main Basement Floor: Poured - Cover or remove tack strips in basement. (Safety item) (Handyman)

7. Main Basement Electrical: 110 VAC - Light fixture shown is hanging by its power wires and should be resecured. (Licensed electrician)

Table of Contents

Definitions	6
General Information	6
Roof	7
Exterior	9
Lots and Grounds	10
Air Conditioning	13
Garage/Carport	14
Heating System	15
Plumbing	17
Electrical	18
Kitchen	19
Laundry Room/Area	21
Bathroom	22
Living Space	23
Bedroom	24
Structure	24
Attic	26
Basement	26
Final Comments	28

Definitions

NOTE: This report has been prepared for the sole and exclusive use of the client indicated above and is limited to an impartial opinion which is not a warranty that the items inspected are defect-free, or that latent or concealed defects may exist as of the date of this inspection or which may have existed in the past or may exist in the future. The report is limited to the components of the property which were visible to the inspector on the date of the inspection and his opinion of their condition at the time of the inspection. Any electrical, plumbing or HVAC work that needs to be done shall be done by a reputable licensed entity in that particular field. All other contractors selected should be reputable with a known history of good service practices.

Acceptable	Functional with no obvious signs of defect.
Not Present	Item not present or not found.
Not Inspected	Item was unable to be inspected for safety reasons or due to lack of power, inaccessible, or disconnected at time of
	inspection.
Maintenance	Item needs normal or periodic maintenance performed to continue to function normally
Minor	Item is not fully functional and requires repair or servicing.
Major	Item needs immediate repair or replacement. It is unable to perform its intended function.

General Information

Property Information

Property Address: Confidential City: State Ohio Zip Inspections/Tests performed: GHI + Radon + WDI + SSI Inspection fee paid:

Client Information

Client Name: Client Address: City: State Zip Phone: Agent Name: Agent Phone: Agent Email:

Inspection Company

Inspector Name Carmen DeLisio Company Name Shooting Star Home Inspections,LLC Inspection Company E-Mail: ShootingStarHomeInspections@gmail.com Inspection Company Phone: 440-478-5363 InterNACHI CPI# 15101906 Ohio Home Inspector License#2019005596 Ohio Radon Tester#RT1000 Ohio Pesticide Applicator License#134512 Ohio Pesticide Business License#105403 FAA Remote Pilot License#4373814

Conditions

Confidential Page 7 of 28

General Information (Continued)

Others Present: None Property Occupied: Occupied Estimated Age of Home: 27 years old Entrance Faces: West Inspection Date: Electric On Yes Gas/Oil On Yes Water On Yes Temperature (F)/Rain in last 3 days? 73/yes Weather at time of inspection: Partly cloudy Soil Conditions Wet Space Below Grade: Basement Building Type: Single family Garage Attached Sewage Disposal: City How Verified Visual Inspection Water Source: City How Verified Visual Inspection

Roof

Entire roof Roof Surface -

- 1. Method of Inspection: Ground with binoculars, ladder at eaves, and aerial drone
- 2. Acceptable Unable to Inspect: 10%
- 3. Acceptable Material: Asphalt shingle
- 4. Acceptable Number of visible shingle layers 1
- 5. Acceptable Visible appearance/condition 1



6. Type: Hip

- 7. Approximate Age: 4 years old
- 8. Acceptable Flashing: Aluminum
- 9. Acceptable Valleys:
- 10. Acceptable Skylights: Insulated glass



Confidential Page 8 of 28

Roof (Continued)

11. Acceptable Plumbing Vents: ABS



- 12. Not Present Electrical Mast: Underground utilities
- 13. Acceptable Gutters: Aluminum
- 14. Acceptable Downspouts: Aluminum
- 15. Acceptable Leader/Extension: Buried
- West Chimney -
- 16. Maintenance Chimney: Brick Chimney crown cracked and should be repaired by a reputable chimney or roofing contractor.



17. Minor

Flue/Flue Cap: Clay - Recommend adding rain/snow cap to round liner at left in picture above in Chimney section.



18. Acceptable

Chimney Flashing: Metal



Confidential Page 9 of 28

Exterior

Whole exterior Exterior Surface

1. Acceptable T



2. Minor

Trim, fascia and soffits: Wood - Peeling paint and possible wood rot or damage to the right hand dormer bottom window frame piece shown. Recommend replacing. (Handyman)



3. Acceptable Door Bell: Hard wired

4. Acceptable Doors: Metal

5. Minor

Siding: Aluminum siding - Recommend handyman repair loose siding shown. A yellow jacket nest was inside the upper siding piece so a specialist may be required to remove the nest and its habitants first and then have the siding repaired. (Handyman and pest specialist)





6. Acceptable7. Acceptable

Windows: Vinyl double hung Exterior Lighting: Pole light and surface mount lights

Confidential Page 10 of 28

Exterior (Continued)

- 8. Acceptable Exterior Electric Outlets: 110 VAC GFCI
- 9. Acceptable Hose Bibs: Gate-frost free type
- 10. Maintenance Gas Meter: Exterior surface mount at left side of home Clear out vegetation all around the meter.



11. Acceptable Electric Meter: Exterior surface mount at rear of home



Lots and Grounds

1. Minor Driveway: Concrete - Driveway is in great shape from apron to garage. Observed a crack by the doors that can be filled with a good quality filler from a DIY store. This will keep the cracks from spreading and deterioration from the freeze - thaw cycles in the winter.



2. Maintenance Walks and steps: Concrete - Some erosion observed on the front steps. This can be repaired by a reputable mason.



Confidential Page 11 of 28


Lots and Grounds (Continued)

3. Acceptable



4. Not Present Patio: 5. Major Deck:

Deck: Stained wood - Consider power washing and staining/painting next season. Steps are a couple inches too high and there are no safety railings present. (Safety item)(Handyman)

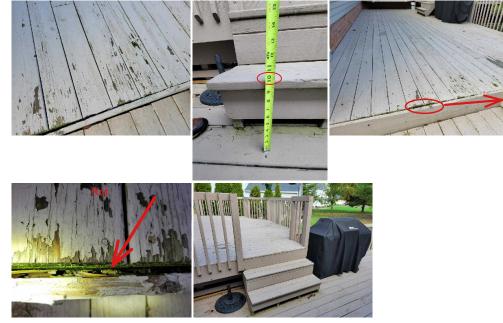

6. Acceptable





Confidential Page 12 of 28

Lots and Grounds (Continued)

7. Acceptable Lot drainage: Adequate slope and depth for drainage - Low point with drain sewer present this is good!



8. Maintenance Vegetation: Trees and shrubs and low vegetation on the perimeter of the home - Trim trees and shrubs away from the structure at least 10-12". Recommend landscape contractor.



- 9. Not Present Window Wells:
- 10. Not Present Retaining Walls:
- 11. Not Inspected Sprinkler system: this is not in the scope of the general inspection



- 12. Not Present Fen
- Fences:

Confidential Page 13 of 28

Air Conditioning

Left side of home AC System -

- 1. Maintenance A/C System Operation: Functional today Recommend reputable licensed HVAC contractor tune-up as no regular servicing evidence was found. Average life of a unit is 15 years. Budget for replacement.
- 2. Acceptable Condensate Removal: PVC
- 3. Acceptable Exterior Unit: Pad mounted



4. Manufacturer: Trane



- 5. Area Served: Whole building Approximate Age: 19 years old
- 6. Type: Central A/C Capacity: 3 Ton
- 7. Acceptable Visible Coil: Aluminum
- 8. Acceptable Refrigerant Lines: Suction line and liquid line
- 9. Acceptable Electrical Disconnect: Fused




Confidential Page 14 of 28

Garage/Carport

Attached Garage -

1. Type of Structure: Attached Car Spaces: 3

2. Minor



3. Minor

Door Openers: Wayne Dalton - Consider changing out the button to a new one that has all of the parts present. (Handyman)



- 4. Acceptable Exterior Surface: Aluminum siding
- 5. Acceptable Roof: Asphalt shingle
- 6. Acceptable Roof Stru


Roof Structure: 2x4 Truss



Doors and windows: Man door to outside has a lock that is inoperative and the door cannot be locked. Recommend repair or replace. (Handyman)



Confidential Page 15 of 28

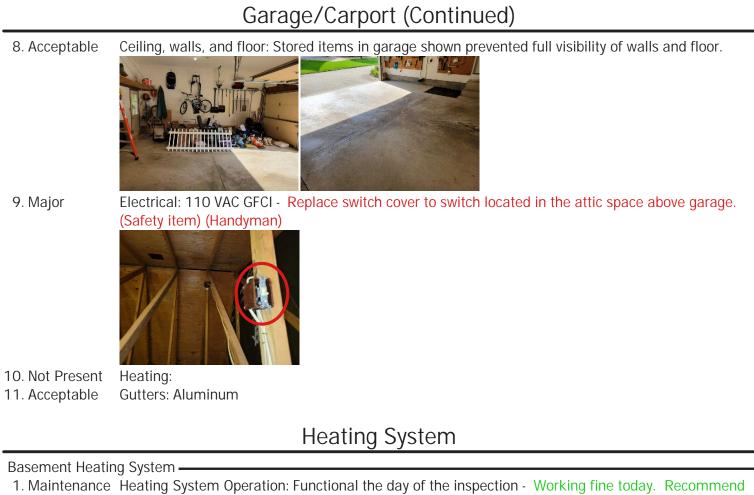

- 1. Maintenance Heating System Operation: Functional the day of the inspection Working fine today. Recommend a licensed HVAC contractor tune-up as the last service on the service tag was 5 years ago.
- 2. Manufacturer: Trane





- 3. Type: Forced air Capacity: 110,000 BTU/hr
- 4. Area Served: Whole building Approximate Age: 7 years old
- 5. Fuel Type: Natural gas
- 6. Not Inspected Heat Exchanger: 5 Burner
- 7. Unable to Inspect: 10%

Confidential Page 16 of 28

Heating System (Continued) 8. Maintenance Filter: Aprilaire - Change filter after you are done moving in. It's due. 9. Acceptable Distribution: Metal duct 10. Not Present Circulator: 11. Acceptable Draft Control: Manual 12. Acceptable Flue Pipe: PVC 13. Maintenance Humidifier: April-Aire - Did not come on when tested. Recommend a licensed HVAC contractor repair and change out the water panel pad. 55 14. Acceptable Thermostats: Living room 70

15. Tank Location: N/A

16. Suspected Asbestos: No

Confidential Page 17 of 28

Plumbing

- 1. Acceptable Service Line: Copper
- 2. Acceptable



- Water Lines: Copper 3. Acceptable
- 4. Acceptable
- 5. Acceptable

Drain Pipes: ABS/PVC

Service Caps: Accessible-basement cleanout shown - Sewer scope was run out to 75 feet. Clean PVC SDR pipe all the way out was observed. No action required.



6. Acceptable Vent Pipes: ABS

7. Acceptable Gas Service Lines: Cast iron

- Basement Water Heater -
- 8. Acceptable Water Heater Operation: Functional at time of inspection
- 9. Manufacturer:



- 10. Type: Tankless Capacity: no limit
- 11. Approximate Age: 7 years old Area Served: Whole building
- Flue Pipe: PVC 12. Acceptable
- 13. Not Present TPRV and Drain Tube:

Confidential Page 18 of 28

Electrical

- 1. Service Size Amps: 150A Volts: 110-240 VAC
- 2. Acceptable Service: Aluminum



- 3. Acceptable 120 VAC Branch Circuits: Copper
- 4. Acceptable 240 VAC Branch Circuits: Aluminum
- 5. Acceptable Wiring: Copper
- 6. Acceptable Ground: Plumbing ground

Basement Electric Panel -

7. Acceptable Panel manufacturer: Square D



- 8. Acceptable
- Main Breaker Size: 150 Amps



9. Acceptable

Breakers: Panel is full-no breakers tripped or off

Confidential Page 19 of 28

Electrical (Continued)

Breakers: (continued)



10. Not PresentFuses:11. Not PresentAFCI:

12. Acceptable GFCI: Present

1st Floor Kitchen -

1. Acceptable

Cooking Appliances: General Electric






Kitchen

Acceptable
 Acceptable

able Exhaust fan: part of microwave able Disposal: In-Sinkerator



Confidential Page 20 of 28

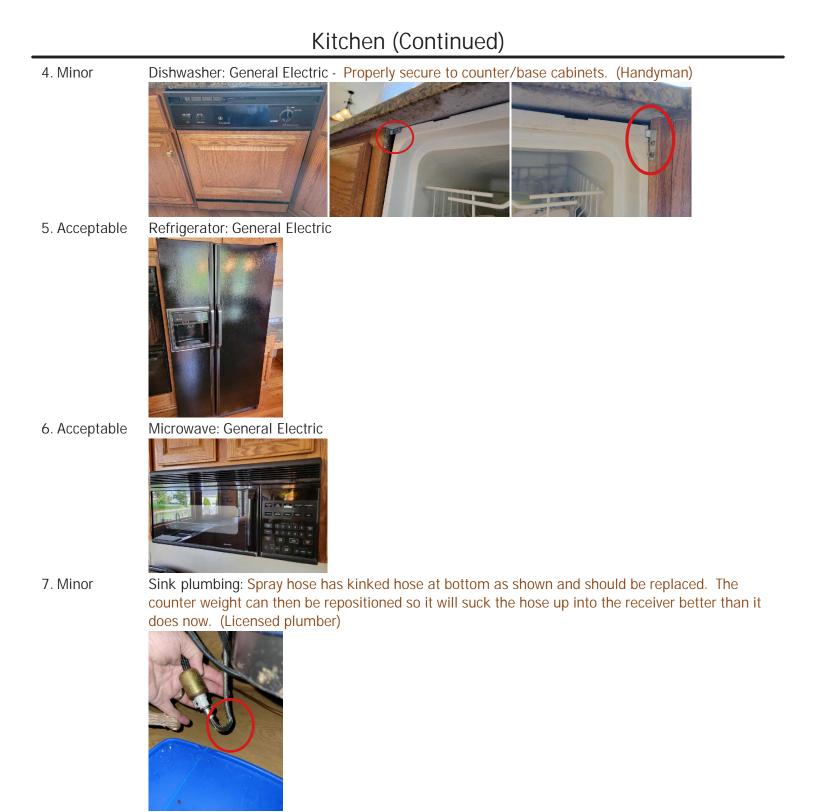

8. Acceptable9. Acceptable10. Acceptable

Electrical: 110 VAC GFCI Cabinets and shelves: Ceiling, walls and floor:

Kitchen (Continued)

11. Acceptable Doors and windows:

12. Acceptable HVAC Source: Heating system register

Laundry Room/Area

1st Floor Laundry Room/Area

- 1. Acceptable Ceiling, walls and floor:
- 2. Acceptable Windows and doors:
- 3. Acceptable HVAC Source: Heating system register
- 4. Acceptable Laundry tub plumbing:
- 5. Acceptable Washer plumbing: Ball valve



6. Acceptable

Washer and Dryer operation: Both LG



7. Acceptable 8. Not Present

Dryer Vent: Metal flex Dryer Gas Line:

9. Acceptable

Dryer Electrical: 220V-4 prong grounded receptacle present



Bathroom

All unless otherwise noted Bathroom -

- 1. Acceptable Walls, ceiling and floor:
- 2. Acceptable Doors and windows:
- 3. Acceptable Electrical: 110 VAC GFCI
- 4. Acceptable Counter/Cabinet:
- 5. Acceptable Sinks, hot/cold water, drains:
- 6. Minor Tubs, hot/cold water, drains: When both hot and cold are turned on the aereator shoots the water to the rear. It probably just needs cleaned. (Handyman)



Acceptable Not Present Minor

e Showers, hot/cold water, drains:

nt Jacuzzi, hot/cold water, drains:

Toilets: The toilet is loose at the floor (front right bedroom bathroom) and will require seal replacement and reinstallation. Fill valve needs replaced as it is spraying water out of the top seal area. (Licensed plumber)



10. Acceptable 11. Acceptable

e HVAC Source:e Ventilation: Electric ventilation fan and window

Confidential Page 23 of 28

Living Space

All unless noted otherwise Living Space -

- 1. Acceptable Walls, ceiling, and floor:
- 2. Major

Doors, windows and trim: Window in first floor office will not stay up and is a safety hazard. Use caution raising and lowering the window until it get repaired or replaced. (Safety item) (Handyman)



3. Not Present 4. Acceptable

Fireplace/Woodstove: Gas/Wood Burning



- 5. Acceptable Stairs/Balcony/Railings:
- Electrical: 110 VAC 6. Acceptable
- 7. Acceptable HVAC Source: Heating system register
- 8. Major

Smoke Detector: Hard wired - Replace any unit over 10 years old even if they test ok as the sensors



9. Not Present CO Detector:

Bedroom

All unless noted otherwise Bedroom -

- 1. Acceptable Closet:
- 2. Minor Ceiling, walls and floor: Carpet burps and seams can be corrected by a carpet professional. The carpet appears to have little wear. Recommend having it stretched and then steam cleaned. Much less cost than replacing it!



Acceptable
 Major

Electrical: 110 VAC - Replace switch cover shown in bedroom. (Safety item)



- 5. Acceptable
- HVAC Source: Heating system register

Structure

1. Acceptable Structure Type: Wood frame

Doors and windows:

2. Acceptable Foundation: Block - Observed one short stair step crack in the foundation block that was filled. Otherwise the foundation looks stellar! Owner reports basement water proofing was done so ask for the paperwork as most of these companies pass the warranties on to future owners.



3. Not Present Differential Movement:

Confidential Page 25 of 28

Structure (Continued)

4. Acceptable Beams: \



5. Acceptable
 6. Acceptable
 7. Acceptable

Bearing Walls: Block/Frame Joists/Trusses: 2x10 Piers/Posts: Steel posts



8. Acceptable

Floor/Slab: Poured slab



9. Acceptable

Subfloor: OSB/Plywood

Attic

Access hatch in bedroom Attic -

- 1. Method of Inspection: Access hatch only
- 2. Acceptable Unable to Inspect: 30%
- 3. Acceptable Roof Framing:



4. Acceptable

5. Acceptable

6. Acceptable

Sheathing: Plywood Ventilation: Ridge and soffit vents Insulation: Blown in



- 7. Not Present Vapor Barrier:
- 8. Not Present Attic Fan:
- 9. Not Present House Fan:
- 10. Acceptable Wiring/Lighting: 110 VAC lighting circuit

Basement

Main Basement -

- 1. Acceptable Unable to Inspect: 25%
- 2. Acceptable Ceiling: Exposed framing and suspended ceiling
- 3. Acceptable Walls: Foundation block and finished off-drywalled
- 4. Major
- Floor: Poured Cover or remove tack strips in basement. (Safety item) (Handyman)



5. Acceptable 6. Acceptable Floor Drain: Surface drain Doors: Bi-fold

Confidential Page 27 of 28



- 11. Not Present
- 12. Acceptable Ventilation: Windows
- 13. Acceptable

Sump Pump: Three sump pump crocks installed - Pumps were cycled and found to be functional today. Battery backup on front single crock was installed and tested functioning fine today.



- 14. Not Present 15. Acceptable 16. Not Present
- Moisture Location: **Basement Stairs/Railings:** Radon mitigation system:

Confidential Page 28 of 28

Final Comments

Good, solid home. Well taken care of!
